




*Establishment of a FramewORk for Transforming current
EPES into a more resilient, reliable and secure system all
over its value chain*

D1.5 Project Management Plan. First update

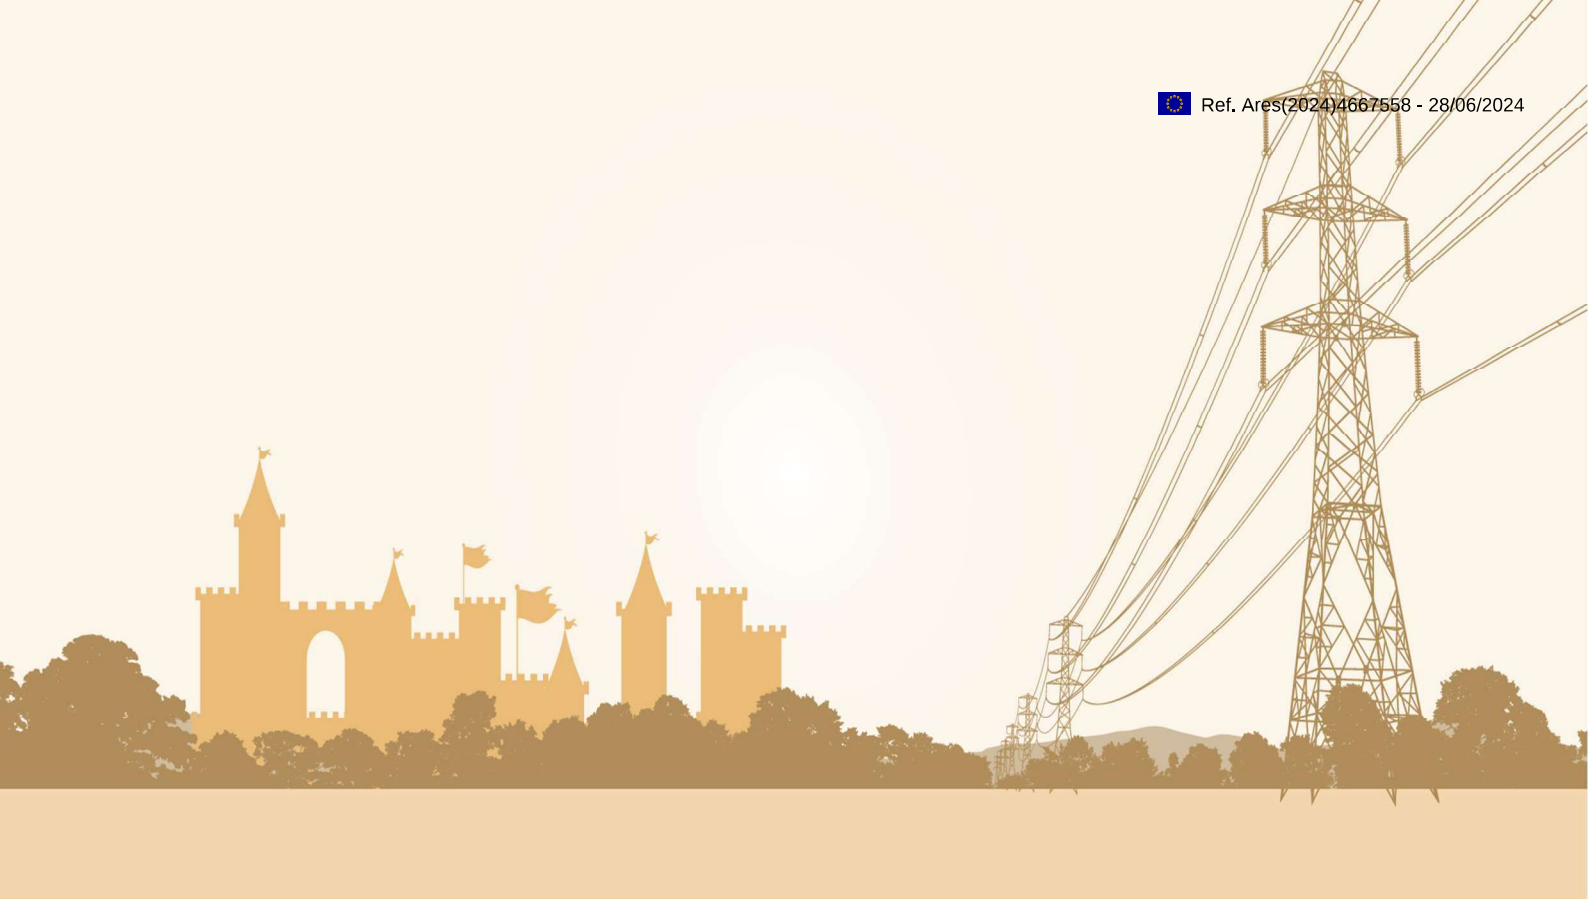

Document details

Deliverable no	D1.5
Deliverable name	Project management Plan. First update
Version	1.0
Release date	28/06/2024
Type	R – Document, report
Dissemination level	SEN - Sensitive
Status	1 st version
Author	CIRCE – Aleida Lostale



DISCLAIMER OF WARRANTIES

This document has been prepared by eFORT project partners as an account of work carried out within the framework of the EC-GA contract no. 101075665.

Neither Project Coordinator, nor any signatory party of eFORT Project Consortium Agreement, nor any person acting on behalf of any of them:

- a) makes any warranty or representation whatsoever, expressed or implied,
 - I. with respect to the use of any information, apparatus, method, process, or similar item disclosed in this document, including merchantability and fitness for a particular purpose, or
 - II. that such use does not infringe on or interfere with privately owned rights, including any party's intellectual property, or
 - III. that this document is suitable to any particular user's circumstance; or
- b) assumes responsibility for any damages or other liability whatsoever (including any consequential damages, even if the Project Coordinator or any representative of a signatory party of the eFORT Project Consortium Agreement has been informed of the possibility of such damages) resulting from your selection or use of this document or any information, apparatus, method, process, or similar item disclosed in this document.

This work has been Funded by the European Union. Views and opinions expressed are however those of the author(s) only and do not necessarily reflect those of the European Union or European Climate, Infrastructure and Environment Executive Agency (CINEA). Neither the European Union nor the granting authority can be held responsible for them.



Document history

Version	Date of issue	Content and changes	Edited by
0.1	11/06/2024	First draft version. Contributions requested to WP leaders	CIRCE
0.2	25/06/2024	Second draft version	WP leaders
1.0	28/06/2024	Final version	CIRCE



Table of contents

Executive summary	10
1 Introduction	11
2 Team composition and roles per entity	11
3 Work Breakdown Structure	14
3.1 WP1 Management and coordination	15
3.1.1 Objectives	15
3.1.2 WP Gantt chart	16
3.1.3 Tasks	16
3.1.4 Milestones	19
3.2 WP2 Analysis and tools for vulnerability, failure, risk and privacy assessment of EPES	20
3.2.1 Objectives	20
3.2.2 WP Gantt chart	20
3.2.3 Tasks	20
3.2.4 Milestones	26
3.3 WP3 Development of technologies for a more secure and robust grid	26
3.3.1 Objectives	26
3.3.2 WP Gantt chart	27
3.3.3 Tasks	27
3.3.4 Milestones	32
3.4 WP4 Development of operational technologies and strategies for increasing grid resiliency	33
3.4.1 Objectives	33
3.4.2 WP Gantt chart	33
3.4.3 Tasks	33
3.4.4 Milestones	38
3.5 WP5 Demonstration trials at eFORT demo-sites	38
3.5.1 Objectives	38
3.5.2 WP Gantt chart	38
3.5.3 Tasks	38
3.5.4 Milestones	43



3.6	WP6 Dissemination, communication and exploitation	43
3.6.1	Objectives	43
3.6.2	WP Gantt chart	44
3.6.3	Tasks	44
3.6.4	Milestones	49
4	Work Packages Interaction.....	50
5	Conclusions.....	51



List of figures

Figure 1 Gantt chart for eFORT project.....	14
Figure 2 Map of Tasks for eFORT project.....	15
Figure 3 WP1 Gantt	16
Figure 4 WP2 Gantt	20
Figure 5 WP3 Gantt	27
Figure 6 WP4 Gantt	33
Figure 7 WP5 Gantt	38
Figure 8 WP6 Gantt	44
Figure 9 eFORT PERT diagram.....	50
List of tablesTable 1 Team composition and roles per entity	11
Table 2 Task 1.1	16
Table 3 Task 1.2.....	17
Table 4 Task 1.3	17
Table 5 Task 1.4	19
Table 6 Task 2.1	20
Table 7 Task 2.2	21
Table 8 Task 2.3.....	22
Table 9 Task 2.4	23
Table 10 Task 2.5	24
Table 11 Task 2.6	24
Table 12 Task 2.7	25
Table 13 Task 3.1	27
Table 14 Task 3.2	28
Table 15 Task 3.3.....	28
Table 16 Task 3.4	29
Table 17 Task 3.5	30
Table 18 Task 3.6	31
Table 19 Task 3.7	32
Table 20 Task 4.1	33
Table 21 Task 4.2	34
Table 22 Task 4.3	35
Table 23 Task 4.4	35



Table 24 Task 4.5	36
Table 25 Task 4.6	37
Table 26 Task 4.7	37
Table 27 Task 5.1	38
Table 28 Task 5.2	39
Table 29 Task 5.3	40
Table 30 Task 5.4	41
Table 31 Task 5.5	41
Table 32 Task 5.6	42
Table 33 Task 5.7	43
Table 34 Task 6.1	44
Table 35 Task 6.2	45
Table 36 Task 6.3	46
Table 37 Task 6.4	47
Table 38 Task 6.5	47
Table 39 Task 6.6	48
Table 40 Task 6.7	49



Abbreviations and Acronyms

Acronym	Description
CBA	Cost Benefit Analysis
D	Deliverable
EPES	Electrical Power and Energy Systems
IC	Intelligent Chatbot
IDS	Intrusion Detection System
IPR	Intellectual Property Rights
OT	Operational Technologies
PMP	Project Management Plan
RRI	Responsible Research and Innovation
SIEM	Security Information and Event Management
WP	Work Package



Executive summary

This deliverable presents the first update of the eFORT Project Management Plan (PMP), released in June 2024 (month 22 of the project) as the natural evolution of the initial version submitted in November 2022 (i.e. D1.2). Conceived as a living document, the PMP is updated periodically to reflect the actual state of consortium agreements regarding planning, responsibilities, task interdependencies and resource allocation. This first update incorporates the progress achieved during the first 20 months of the project, providing a revised description of the team composition and roles per entity, an updated Gantt chart and Work Breakdown Structure, and refined objectives, tasks and milestones for each of the 6 Work Packages. The document also describes the interactions between Work Packages and reports on the minor adjustments performed in the distribution of efforts among partners. By consolidating all these updates in a single reference document, D1.5 ensures that the consortium continues to operate under a common and up-to-date framework, minimising misunderstandings, optimising the use of resources and keeping eFORT activities fully aligned with the Grant Agreement.

