


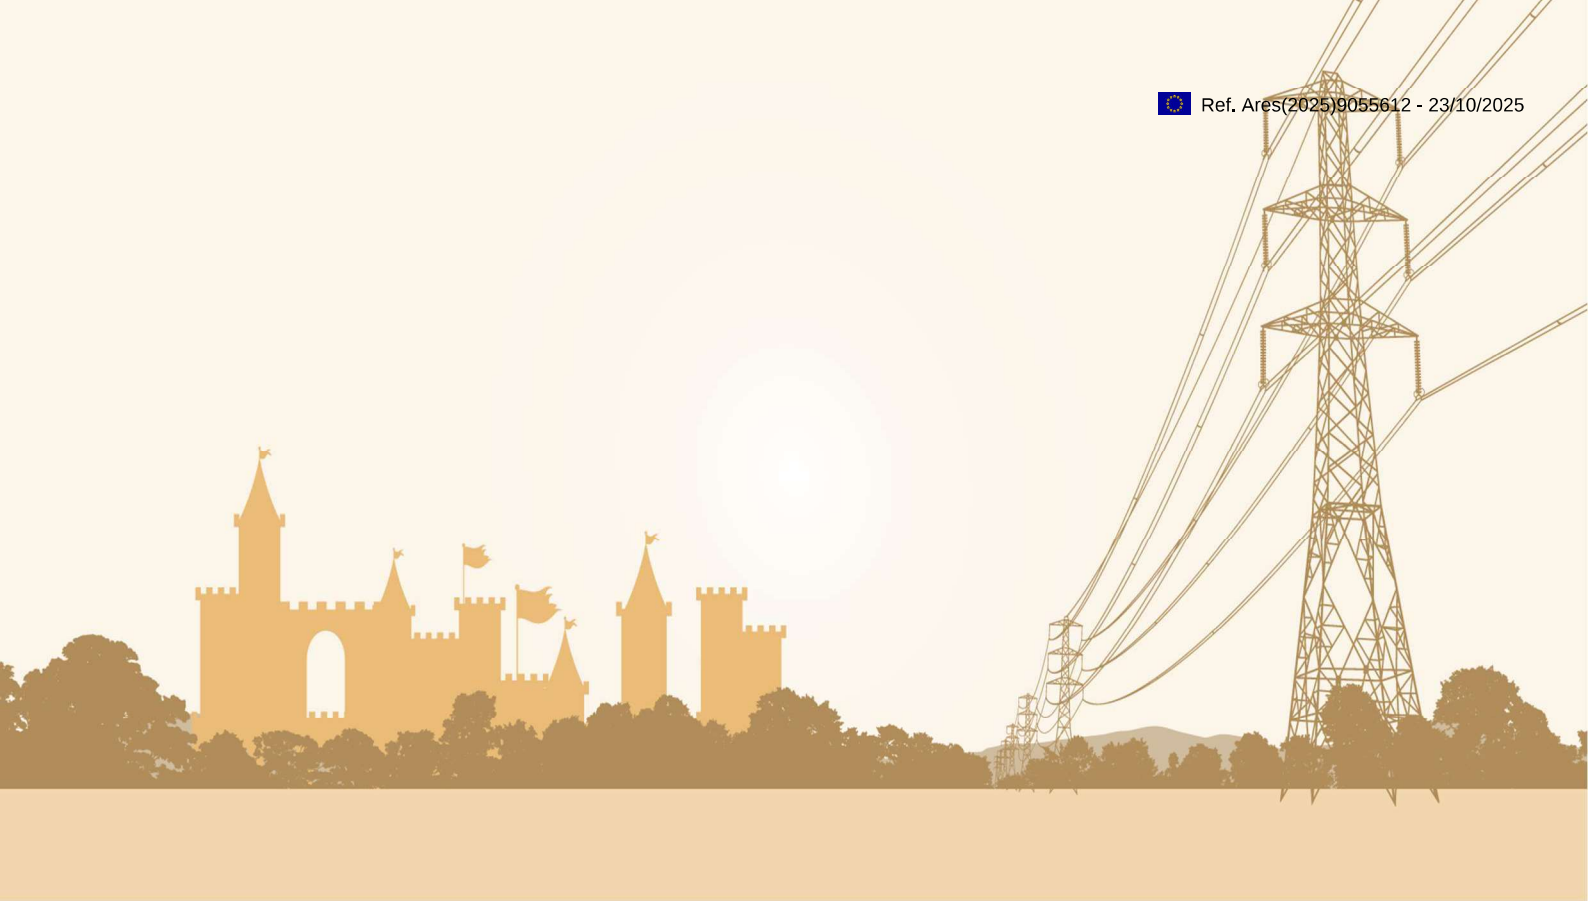

*Establishment of a FramewORk for Transforming current
EPES into a more resilient, reliable and secure system all
over its value chain*

D1.7 Project Management Plan. Second update

Document details

Deliverable no	D1.7
Deliverable name	Project management Plan. Second update
Version	0.1
Release date	23/10/2025
Type	R – Document, report
Dissemination level	SEN - Sensitive
Status	Final version
Author	CIRCE – Aleida Lostale



DISCLAIMER OF WARRANTIES

This document has been prepared by eFORT project partners as an account of work carried out within the framework of the EC-GA contract no. 101075665.

Neither Project Coordinator, nor any signatory party of eFORT Project Consortium Agreement, nor any person acting on behalf of any of them:

- a) makes any warranty or representation whatsoever, expressed or implied,
 - I. with respect to the use of any information, apparatus, method, process, or similar item disclosed in this document, including merchantability and fitness for a particular purpose, or
 - II. that such use does not infringe on or interfere with privately owned rights, including any party's intellectual property, or
 - III. that this document is suitable to any particular user's circumstance; or
- b) assumes responsibility for any damages or other liability whatsoever (including any consequential damages, even if the Project Coordinator or any representative of a signatory party of the eFORT Project Consortium Agreement has been informed of the possibility of such damages) resulting from your selection or use of this document or any information, apparatus, method, process, or similar item disclosed in this document.

This work has been Funded by the European Union. Views and opinions expressed are however those of the author(s) only and do not necessarily reflect those of the European Union or European Climate, Infrastructure and Environment Executive Agency (CINEA). Neither the European Union nor the granting authority can be held responsible for them.



Document history

Version	Date of issue	Content and changes	Edited by
0.0	22/08/2025	First draft version. Contributions requested to WP leaders	CIRCE
0.1	23/10/2025	Final version	Project Consortium



Table of contents

Executive summary	10
1 Introduction	11
2 Team composition and roles per entity	11
3 Work Breakdown Structure	14
3.1 WP1 Management and coordination	16
3.1.1 Objectives	16
3.1.2 WP Gantt chart	16
3.1.3 Tasks	16
3.1.4 Milestones	20
3.2 WP2 Analysis and tools for vulnerability, failure, risk and privacy assessment of EPES	20
3.2.1 Objectives	20
3.2.2 WP Gantt chart	20
3.2.3 Tasks	20
3.2.4 Milestones	26
3.3 WP3 Development of technologies for a more secure and robust grid	26
3.3.1 Objectives	26
3.3.2 WP Gantt chart	27
3.3.3 Tasks	27
3.3.4 Milestones	32
3.4 WP4 Development of operational technologies and strategies for increasing grid resiliency	32
3.4.1 Objectives	32
3.4.2 WP Gantt chart	33
3.4.3 Tasks	33
3.4.4 Milestones	37
3.5 WP5 Demonstration trials at eFORT demo-sites	37
3.5.1 Objectives	37
3.5.2 WP Gantt chart	37
3.5.3 Tasks	38
3.5.4 Milestones	42



3.6	WP6 Dissemination, communication and exploitation	43
3.6.1	Objectives	43
3.6.2	WP Gantt chart	43
3.6.3	Tasks	44
3.6.4	Milestones	48
4	Work Packages Interaction.....	48
5	Conclusions.....	50
6	Annex 1: Summary of project deliverables status	52
7	Annex 2: Summary of project milestones status	55



List of figures

Figure 1 Gantt chart for eFORT project.....	15
Figure 2 Map of Tasks for eFORT project.....	15
Figure 3 WP1 Gantt.....	16
Figure 4 WP2 Gantt.....	20
Figure 5 WP3 Gantt.....	27
Figure 6 WP4 Gantt.....	33
Figure 7 WP5 Gantt.....	38
Figure 8 WP6 Gantt.....	43
Figure 9 eFORT PERT diagram.....	50

List of tables

Table 1 Team composition and roles per entity.....	11
Table 2 Information of Task 1.1	16
Table 3 Information of Task 1.2	17
Table 4 Information of Task 1.3	18
Table 5 Information of Task 1.4	19
Table 6 Information of Task 2.1	20
Table 7 Information of Task 2.2	21
Table 8 Information of Task 2.3	22
Table 9 Information of Task 2.4	23
Table 10 Information of Task 2.5	23
Table 11 Information of Task 2.6	24
Table 12 Information of Task 2.7	25
Table 13 Information of Task 3.1	27
Table 14 Information of Task 3.2	28
Table 15 Information of Task 3.3	28
Table 16 Information of Task 3.4	29
Table 17 Information of Task 3.5	30
Table 18 Information of Task 3.6	30
Table 19 Information of Task 3.7	31
Table 20 Information of Task 4.1	33
Table 21 Information of Task 4.2	33



Table 22 Information of Task 4.3	34
Table 23 Information of Task 4.4	35
Table 24 Information of Task 4.5	35
Table 25 Information of Task 4.6	36
Table 26 Information of Task 4.7	36
Table 27 Information of Task 5.1	38
Table 28 Information of Task 5.2	38
Table 29 Information of Task 5.3	39
Table 30 Information of Task 5.4	40
Table 31 Information of Task 5.5	41
Table 32 Information of Task 5.6	41
Table 33 Information of Task 5.7	42
Table 34 Information of Task 6.1	44
Table 35 Information of Task 6.2	44
Table 36 Information of Task 6.3	45
Table 37 Information of Task 6.4	46
Table 38 Information of Task 6.5	46
Table 39 Information of Task 6.6	47
Table 40 Information of Task 6.7	48
Table 41 Summary of project deliverables status	52
Table 42 Summary of project milestones status	55



Abbreviations and Acronyms

Acronym	Description
CBA	Cost Benefit Analysis
D	Deliverable
EPES	Electrical Power and Energy Systems
IC	Intelligent Chatbot
IDS	Intrusion Detection System
IPR	Intellectual Property Rights
OT	Operational Technologies
PMP	Project Management Plan
RRI	Responsible Research and Innovation
SIEM	Security Information and Event Management
WP	Work Package



Executive summary

This deliverable provides the second update of the eFORT Project Management Plan (PMP), offering a consolidated view of how the project is being steered at month 38 (i.e. October 2025), after the initial version (D1.2 submitted in November 2022) and the first update (D1.5 submitted in June 2024). It records the current state of consortium organisation, responsibilities, planning, and reporting mechanisms, ensuring that all partners operate under a common and up-to-date framework. The document highlights the progress made since the previous version, including refinements in task scheduling, milestones and resource allocation, and presents a revised description of the team composition and roles per entity, an updated Gantt chart and Work Breakdown Structure, and the objectives and milestones for each of the 6 Work Packages, together with the description of their interactions. Two dedicated annexes summarise the status of all project deliverables and milestones, providing a complete overview of the achievements consolidated towards the final stages of the project. By presenting this updated PMP, the consortium reinforces a shared understanding of project execution, alignment with the Grant Agreement, and preparedness for the closing phase, reaffirming the PMP as a living document that ensures eFORT's activities are coordinated efficiently and directed towards delivering its expected impact on the resilience and security of Europe's energy systems.

