Ref. Ares(2022)8206548 - 28/11/2022

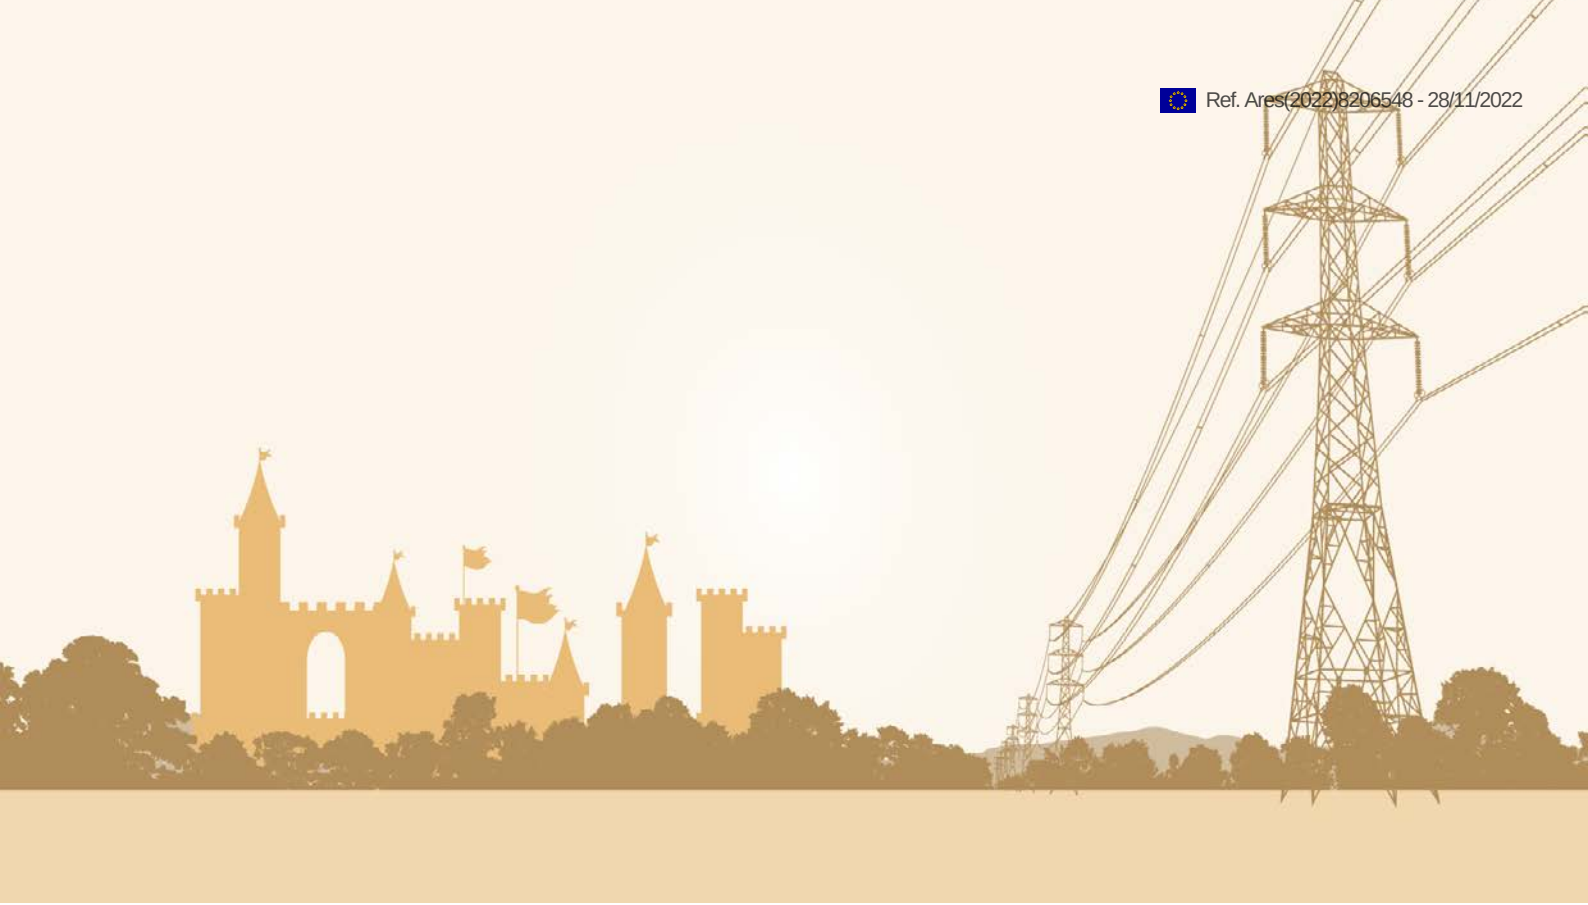

eFORT

Establishment of a FramewORk for Transforming current EPES into a more resilient, reliable and secure system all over its value chain

D1.2 Project Management Plan. Initial Version

Document details

Deliverable no	D1.2
Deliverable name	Project management Plan. Initial Version
Version	1.0
Release date	28/11/2022
Type	R
Dissemination level	SEN
Status	Final Version
Author	CIRCE – Alfonso Bernad

DISCLAIMER OF WARRANTIES

This document has been prepared by eFORT project partners as an account of work carried out within the framework of the EC-GA contract no. 101075665.

Neither Project Coordinator, nor any signatory party of eFORT Project Consortium Agreement, nor any person acting on behalf of any of them:

a) makes any warranty or representation whatsoever, expressed or implied,

   I. with respect to the use of any information, apparatus, method, process, or similar item disclosed in this document, including merchantability and fitness for a particular purpose, or

   II. that such use does not infringe on or interfere with privately owned rights, including any party's intellectual property, or

   III. that this document is suitable to any particular user's circumstance; or

b) assumes responsibility for any damages or other liability whatsoever (including any consequential damages, even if the Project Coordinator or any representative of a signatory party of the eFORT Project Consortium Agreement has been informed of the possibility of such damages) resulting from your selection or use of this document or any information, apparatus, method, process, or similar item disclosed in this document.

This work has been Funded by the European Union. Views and opinions expressed are however those of the author(s) only and do not necessarily reflect those of the European Union or European Climate, Infrastructure and Environment Executive Agency (CINEA). Neither the European Union nor the granting authority can be held responsible for them.

Document history

Version	Date of issue	Content and changes	Edited by
0.1	09/11/2022	First draft version and contributions request to WPleaders	CIRCE
0.2	25/11/2022	Contributions for WPleaders included	CIRCE
1.0	28/11/2022	Final version to be submitted	CIRCE

Table of contents

Executive summary **10**

1 Introduction **11**

2 Team composition and roles per entity **11**

3 Work Breakdown Structure **14**

3.1 WP1 Management and coordination 15

3.1.1 Objectives 15

3.1.2 WP Gantt chart 15

3.1.3 Tasks 16

3.1.4 Milestones 19

3.2 WP2 Analysis and tools for vulnerability, failure, risk and privacy assessment of EPES 20

3.2.1 Objectives 20

3.2.2 WP Gantt chart 20

3.2.3 Tasks 21

3.2.4 Milestones 28

3.3 WP3 Development of technologies for a more secure and robust grid 29

3.3.1 Objectives 29

3.3.2 WP Gantt chart 29

3.3.3 Tasks 30

3.3.4 Milestones 36

3.4 WP4 Development of operational technologies and strategies for increasing grid resiliency 37

3.4.1 Objectives 37

3.4.2 WP Gantt chart 37

3.4.3 Tasks 37

3.4.4 Milestones 44

3.5 WP5 Demonstration trials at eFORT demo-sites 44

3.5.1 Objectives 44

3.5.2 WP Gantt chart 45

3.5.3 Tasks 45
3.5.4 Milestones 51
3.6 WP6 Dissemination, communication and exploitation 51
3.6.1 Objectives 51
3.6.2 WP Gantt chart 52
3.6.3 Tasks 52
3.6.4 Milestones 59

4 Work Packages Interaction 59

5 Conclusions 60

List of figures

Figure 2 Gantt chart for the eFORT project 14
Figure 3 WP1 Gantt 15
Figure 4 WP2 Gantt 20
Figure 5 WP3 Gantt 29
Figure 6 WP4 Gantt 37
Figure 7 WP5 Gantt 45
Figure 8 WP6 Gantt 52
Figure 9 eFORT WPs 60

List of tables

Table 1 Team composition and roles per entity 11
Table 2 Task 1.1 16
Table 3 Task 1.2 17
Table 4 Task 1.3 18
Table 5 Task 1.4 19
Table 6 Task 2.1 21
Table 7 Task 2.2 22
Table 8 Task 2.3 24
Table 9 Task 2.4 25
Table 10 Task 2.5 26
Table 11 Task 2.6 27
Table 12 Task 2.7 28
Table 13 Task 3.1 30
Table 14 Task 3.2 31
Table 15 Task 3.3 32
Table 16 Task 3.4 33
Table 17 Task 3.5 34
Table 18 Task 3.6 35
Table 19 Task 3.7 36
Table 20 Task 4.1 38
Table 21 Task 4.2 39
Table 22 Task 4.3 40
Table 23 Task 4.4 41

Table 24 Task 4.5 42
Table 25 Task 4.6 43
Table 26 Task 4.7 44
Table 27 Task 5.1 45
Table 28 Task 5.2 46
Table 29 Task 5.3 47
Table 30 Task 5.4 48
Table 31 Task 5.5 49
Table 32 Task 5.6 50
Table 33 Task 5.7 51
Table 34 Task 6.1 53
Table 35 Task 6.2 54
Table 36 Task 6.3 55
Table 37 Task 6.4 56
Table 38 Task 6.5 57
Table 39 Task 6.6 58
Table 40 Task 6.7 59

Abbreviations and Acronyms

Acronym	Description
CBA	Cost Benefit Analysis
D	Deliverable
EPES	Electrical Power and Energy Systems
IC	Intelligent Chatbot
IDS	Intrusion Detection System
IPR	Intellectual Property Rights
OT	Operational Technologies
PMP	Project Management Plan
RRI	Responsible Research and Innovation
SIEM	Security Information and Event Management
WP	Work Package

Executive summary

This deliverable presents the first version of the eFORT Project Management Plan (PMP), the central planning instrument that aligns all 23 partners towards the common goals of the project. The document introduces the team composition and the specific role of each entity in the consortium, and details the Work Breakdown Structure of the 6 Work Packages (WP) that build the project, from the analysis of vulnerabilities and risks in EPES (WP2), through the development of cyber and physical technologies for a more secure and robust grid (WP3) and operational strategies for grid resiliency (WP4), to the demonstration trials at the four demo-sites (WP5) and the dissemination, communication and exploitation activities (WP6), all coordinated under WP1. For each WP, the PMP defines the objectives, the Gantt chart, the breakdown into tasks and the associated milestones, as well as the interactions between Work Packages. Conceived as a living document, this initial PMP minimises misunderstandings and optimises the use of resources, providing a comprehensive baseline that each partner can rely on to further develop its methods and strategies throughout the project lifetime.
